Sakthi Automotive Group - Quality Command

MONTHLY REJECTION & QUALITY COST REPORT • Period: **2026-11** • Generated: 06-Nov-2026 15:34

TOTAL PLANT PRODUCTION	TOTAL REJECTED CASTINGS	PLANT REJECTION %	TOTAL QUALITY LOSS (COP)
16,288	471	2.89%	INR 97,435
Output Target: 16,440	Defect Count	Control Limit: 2.80%	Cost of Poor Quality


Monthly Quality Assessment & CAPA Directions

- Monthly plant-wide production reached 16,288 components with total rejections at 2.89%.
- Cumulative Cost of Poor Quality (COP) totaled INR 97,435 across all divisions.
- Foundry and Machine Shop defect Pareto shows top 3 defect classifications account for >60% of plant losses.
- CAPA Focus: Molding sand moisture stabilization and CNC tool insert replacement cycles.

1. Division Quality Performance Summary

Division	Shop Description	Produced Pcs	Accepted Pcs	Rejected Pcs	Rejection %	Yield %	Status
FOUNDRY	Automotive Casting Foundry Division	12,628	12,213	415	**3.29%**	96.71%	In Control
MACHINE_SHOP	Precision Machining & CNC Division	3,660	3,604	56	**1.53%**	98.47%	In Control

2. Plant-Wide Defect Pareto Analysis

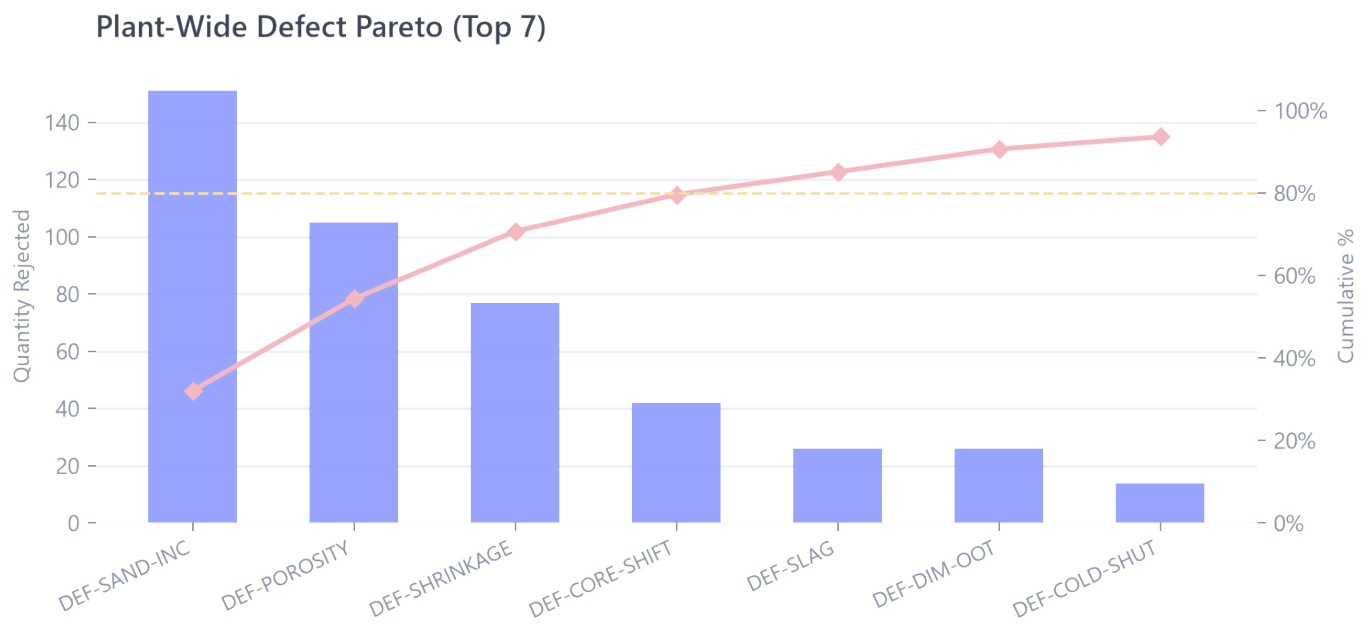

Shop	Defect Code	Defect Description	Category	Rejected Pcs	Scrap Loss Cost	% Share	Cumulative %
FOUNDRY	**DEF-SAND-INC**	Sand Inclusion / Mold Erosion	MOLDING	151	INR 26,230	32.1%	**32.1%**
FOUNDRY	**DEF-POROSITY**	Gas Porosity / Pin Holes	METALLURGICAL	105	INR 22,405	22.3%	**54.4%**
FOUNDRY	**DEF-SHRINKAGE**	Shrinkage Cavity / Porosity	METALLURGICAL	77	INR 19,970	16.3%	**70.7%**
FOUNDRY	**DEF-CORE-SHIFT**	Core Shift / Wall Thinning	CORE_MAKING	42	INR 9,920	8.9%	**79.6%**
FOUNDRY	**DEF-SLAG**	Slag / Dross Inclusion	POURING	26	INR 5,920	5.5%	**85.1%**
MACHINE_SHOP	**DEF-DIM-OOT**	Dimensional Out of Tolerance	MACHINING	26	INR 3,405	5.5%	**90.7%**
FOUNDRY	**DEF-COLD-SHUT**	Cold Shut / Incomplete Pour	POURING	14	INR 2,590	3.0%	**93.6%**
MACHINE_SHOP	**DEF-RUNOUT**	Face Runout / Dynamic Wobble	MACHINING	8	INR 1,180	1.7%	**95.3%**
MACHINE_SHOP	**DEF-SUB-POR**	Subsurface Casting Porosity revealed	RAW_MATERIAL	8	INR 3,010	1.7%	**97.0%**
MACHINE_SHOP	**DEF-SURF-CHAT**	Surface Roughness / Chatter Marks	TOOLING	6	INR 885	1.3%	**98.3%**
MACHINE_SHOP	**DEF-BURR**	Heavy Burr / Incomplete Chamfer	DEBURRING	4	INR 0	0.8%	**99.2%**
MACHINE_SHOP	**DEF-TOOL-BRK**	Drill / Tap Breakage inside part	TOOLING	4	INR 1,920	0.8%	**100.0%**
